



August 7, 2019

Dear Members and Friends of the Hills Church,


The Parish House HVAC and renovation project has been moving along, as you will see from the descriptions and photos below. The project is still on track to complete the work in the Nursery School area by 8/23 so that they can begin classes on schedule in September. Note that work in the second and third floors is scheduled to be completed in the Fall.

On the Nursery School floor, the fire protection main lines, branch piping, and most of fire protection heads (sprinklers) have been installed.



In addition, Fraser, the HVAC subcontractor, has been insulating the hot water pipes on this floor.

The carpenters have been framing and boarding the soffits around the windows on the first floor which are being primed and painted this week. The installation of the light fixtures and new ceiling grid and tiles are scheduled to begin the week of 8/5.

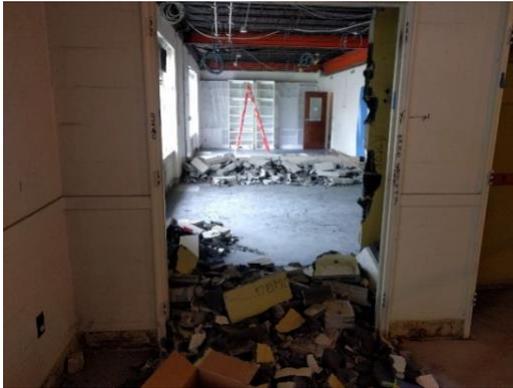

On the second (office) floor, the wall between the vestibule and the administrator's office, and the wall between the latter and the library have been demo-ed in preparation for re-configuring the spaces to create an administrator's office which faces the vestibule, and a financial office. Fraser also began to pull the AC lines on this floor.

On the third floor (Sunday School), Fraser cored holes through the slab in order to run piping.



Just as a reminder, these construction updates from the moderators are also appearing on the church's website in case you should miss one: <https://www.hillschurch.org/news/> . The next update will be in two weeks. Meanwhile, should you have any questions or concerns, please do not hesitate to contact any of the Moderators individually or by email: officeofthemoderator@hillschurch.org.

In service and faith,

Mary Hill Canavan, Gintas Vildzius, Christopher Stowell

Office of the Moderator
